



The Harvest Golf Club Irrigation Install Update: May 8th

Reparation work initiated around the pumphouse is near completion. This is located to the right of the 9th fairway (see image #1 taken on May 7th). Any remaining excavated areas have been refilled and covered with nice sand material to ensure that the ground can properly compact before new sod is installed. This process prevents any potential future uneven ground in the area when settling.




the initial phase of directional drilling, dating back to April 3rd was successfully completed, this phase entailed the installation of 10 and 8 inch pipe. During this process very hard soil was encountered and the drilling process was slowed down to prevent damage to this equipment or the golf course.

Starting the drilling in the general area of the clubhouse and pumphouse means there are many electrical conduits under ground connecting the clubhouse, kiosk, pumphouse, and waterfall in the retaining pond between the 5th and 9th fairway. Consequently, the initial drilling process reached 4-5 feet into the ground to avoid all electrical conduits. Additionally, this different depth meant that reinforced pipe connectors needed to be ordered to ensure solidity and longevity of these connections.

AP Irrigation is scheduled to resume work Thursday May 9th. Moving forward directional drilling will continue in the direction of the 7th green, 8 tee, and behind #16 and #7(see Image #3 below). We anticipate the work in this general area to take a few weeks to complete. A further update will be provided to you in the first week of June that will provide you with the next drilling direction/areas. As we travel further away from the pumphouse the size of pipe inserted into the ground will now shift to 6 to 4 inches in diameter. It is suggested by AP Irrigation that the drilling process should become easier. However, as this is a one of a kind project, only when into the ground will we know how long each sections of the golf course may take to complete.

Should everything planned remain on schedule the mainline pipe installations should be completed around Oct 1st. We would also hope, schedule/ weather permitting, to begin the installation of lateral lines/sprinkler head installation on selected holes before the frost season and winter sets in.

*expected project timelines are condition dependant and may vary. Our aim is to to keep you informed throughout the process and we will make every effort to notify you of any unforeseen changes.

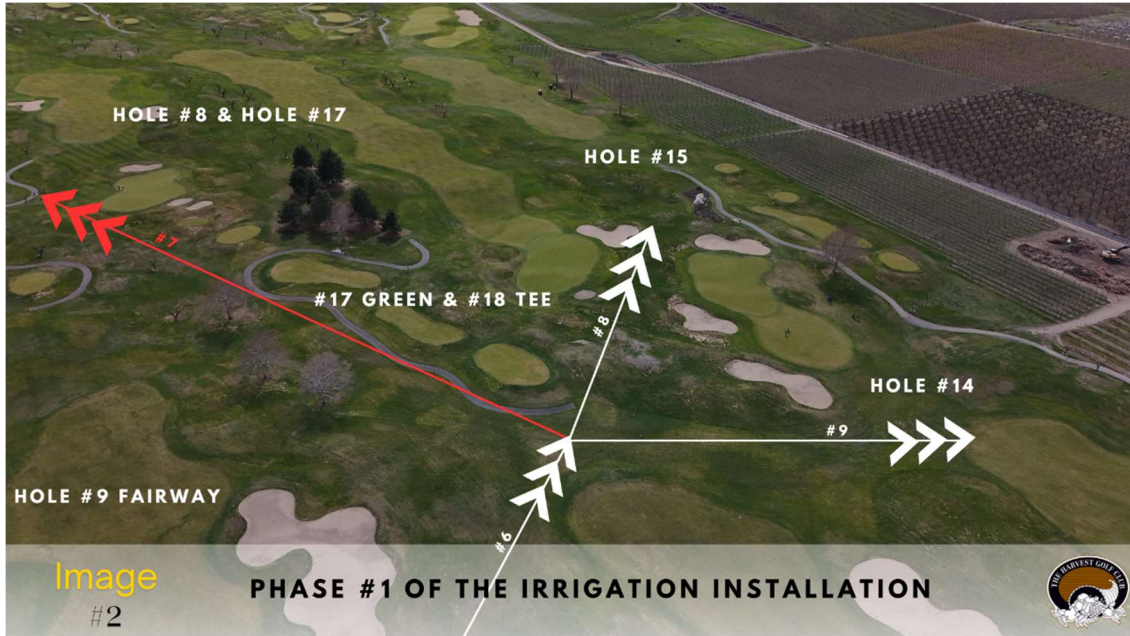

We would like to thank you once more for your patience and understanding as this entire project may be considered construction work while play is in progress.

Due to the intricacies of the scope of work, it may be inevitable for the AP Irrigation team to avoid generating background noise or at times be in the general area of play. We respectfully request for your cooperation by exercising care as they are strictly performing their necessary duties and we need to keep

the team at AP Irrigation safe. If during play your golf ball ever finds its way near excavated holes that have been roped off please keep your distance to avoid any possible please refrain from being near to avoid any possible accident that could occur.

Should you have ever have a question about this new irrigation install, please do not hesitate to contact me via phone or stop by my office at any time of your choosing.

With the utmost respect,
Gilles Dufort
General Manager / Executive Professional
The Harvest Golf Club
